




# NEW ADMINISTRATION BUILDING



Northern parking lot pour has been completed. Site work has been delayed due to rain.

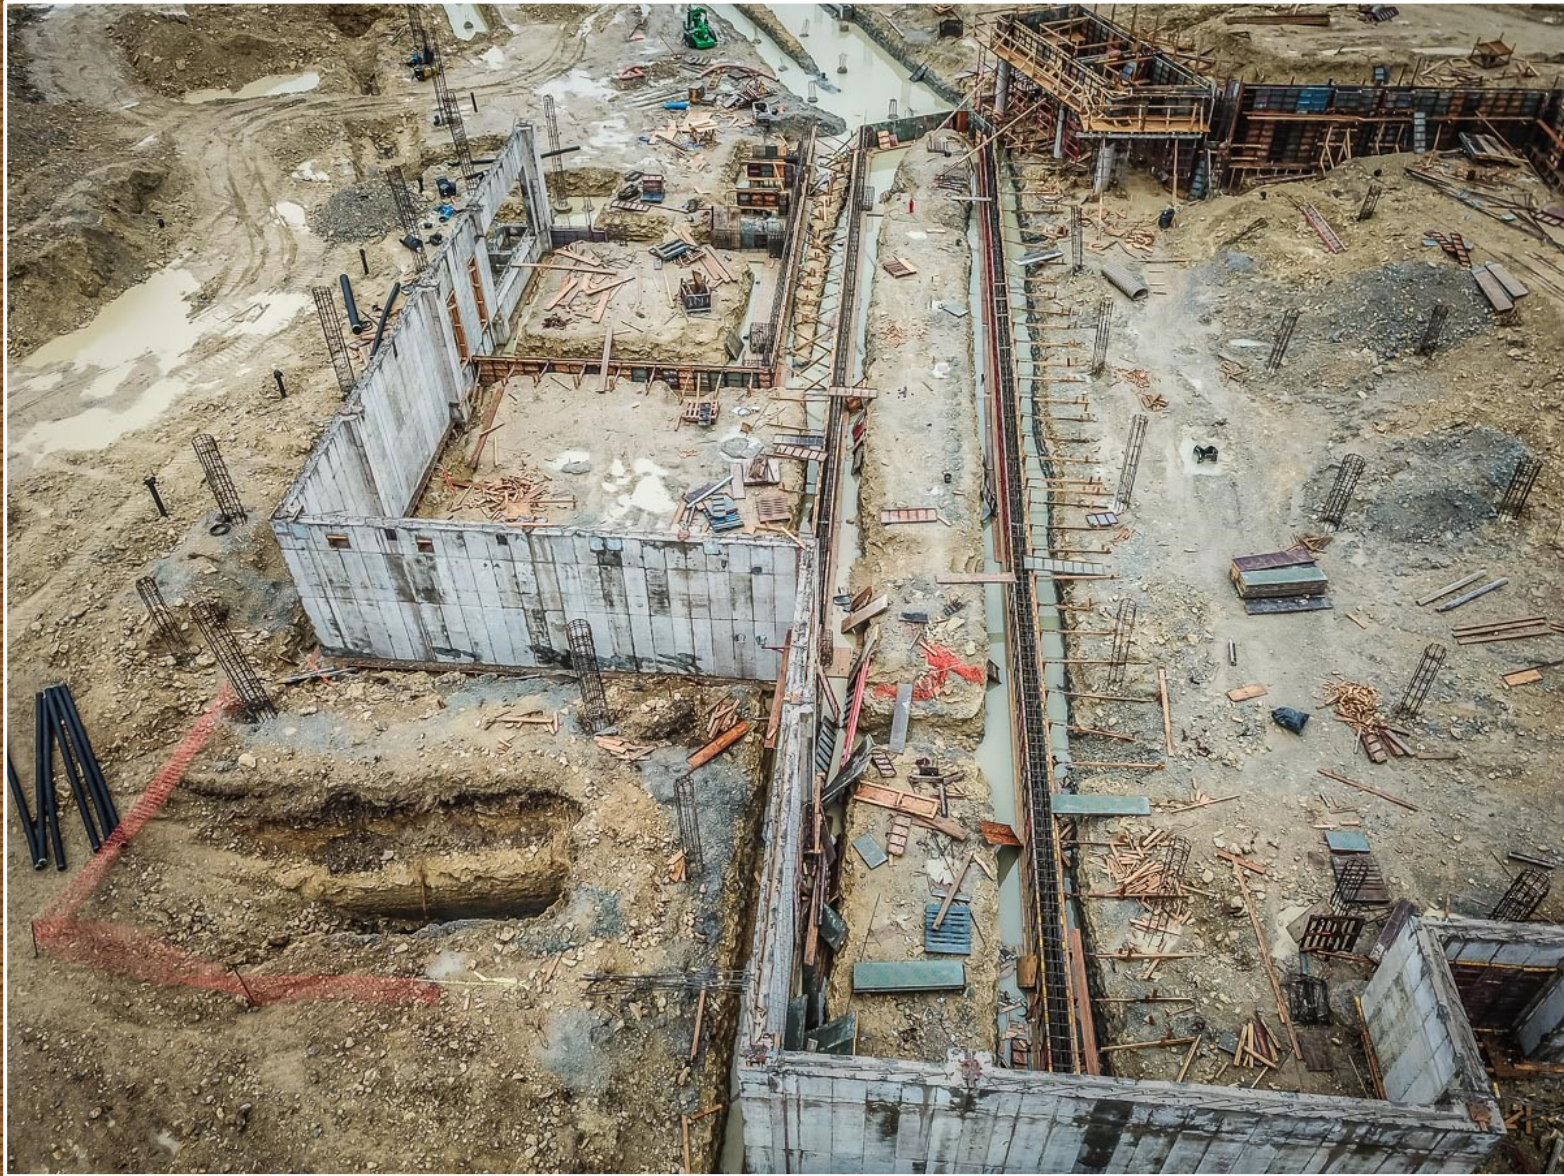

Eastern walls in the business area are being formed up for future concrete pour.




# BOSWELL HS

Stadium grandstand is scheduled for arrival July 2.





**Stadium masonry columns have been completed.**

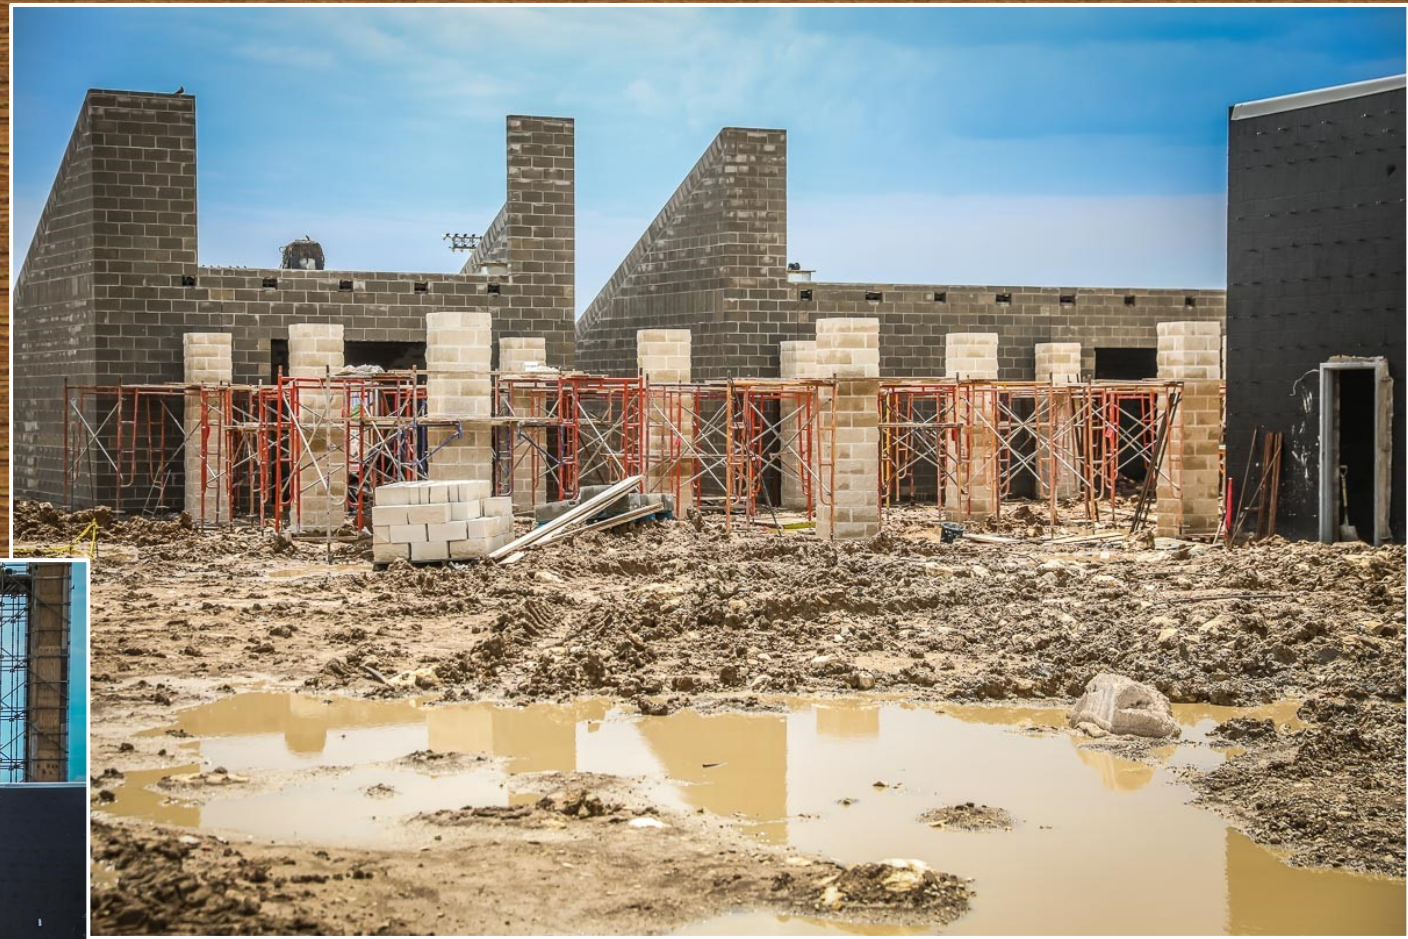


**Concrete flatwork needs to be completed before the grandstand's installation can proceed.**



**Metal studs are on backorder due to supply issues.**



**Light poles have arrived on site and visitor bleacher pier drilling has resumed. Needs to be completed by June 16.**

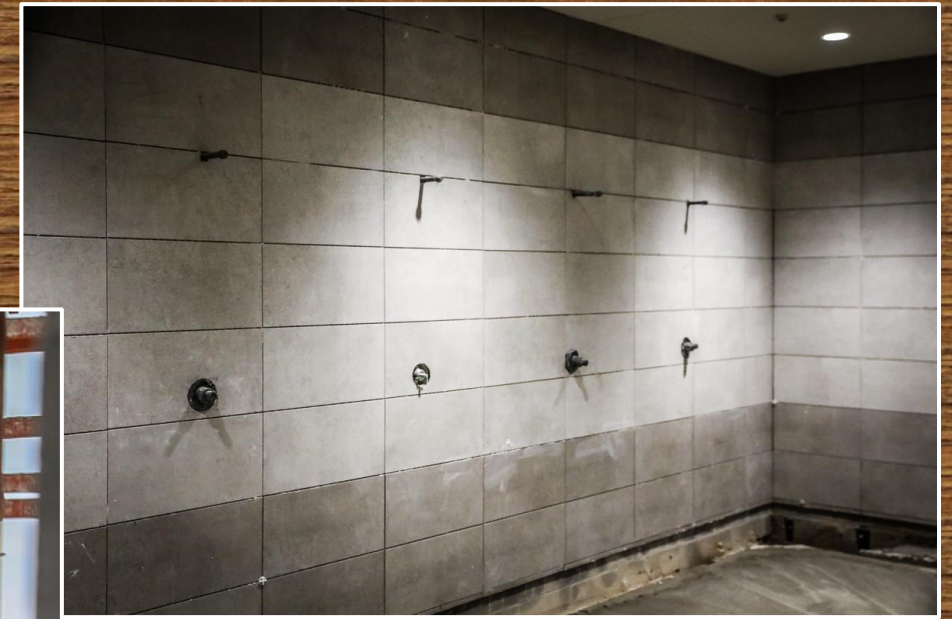

**CMU block work is near completion on the visitor's side ticket booth. Wall tile work in the shower rooms has been completed.**




**Interior renovation of the gymnastics area includes expanding the storage areas, public restrooms, new locker rooms and lockers, new offices, fire sprinkler installed, LED lighting, and painting.**



# LAKE COUNTRY ES


Kitchen is ready for final cleaning.

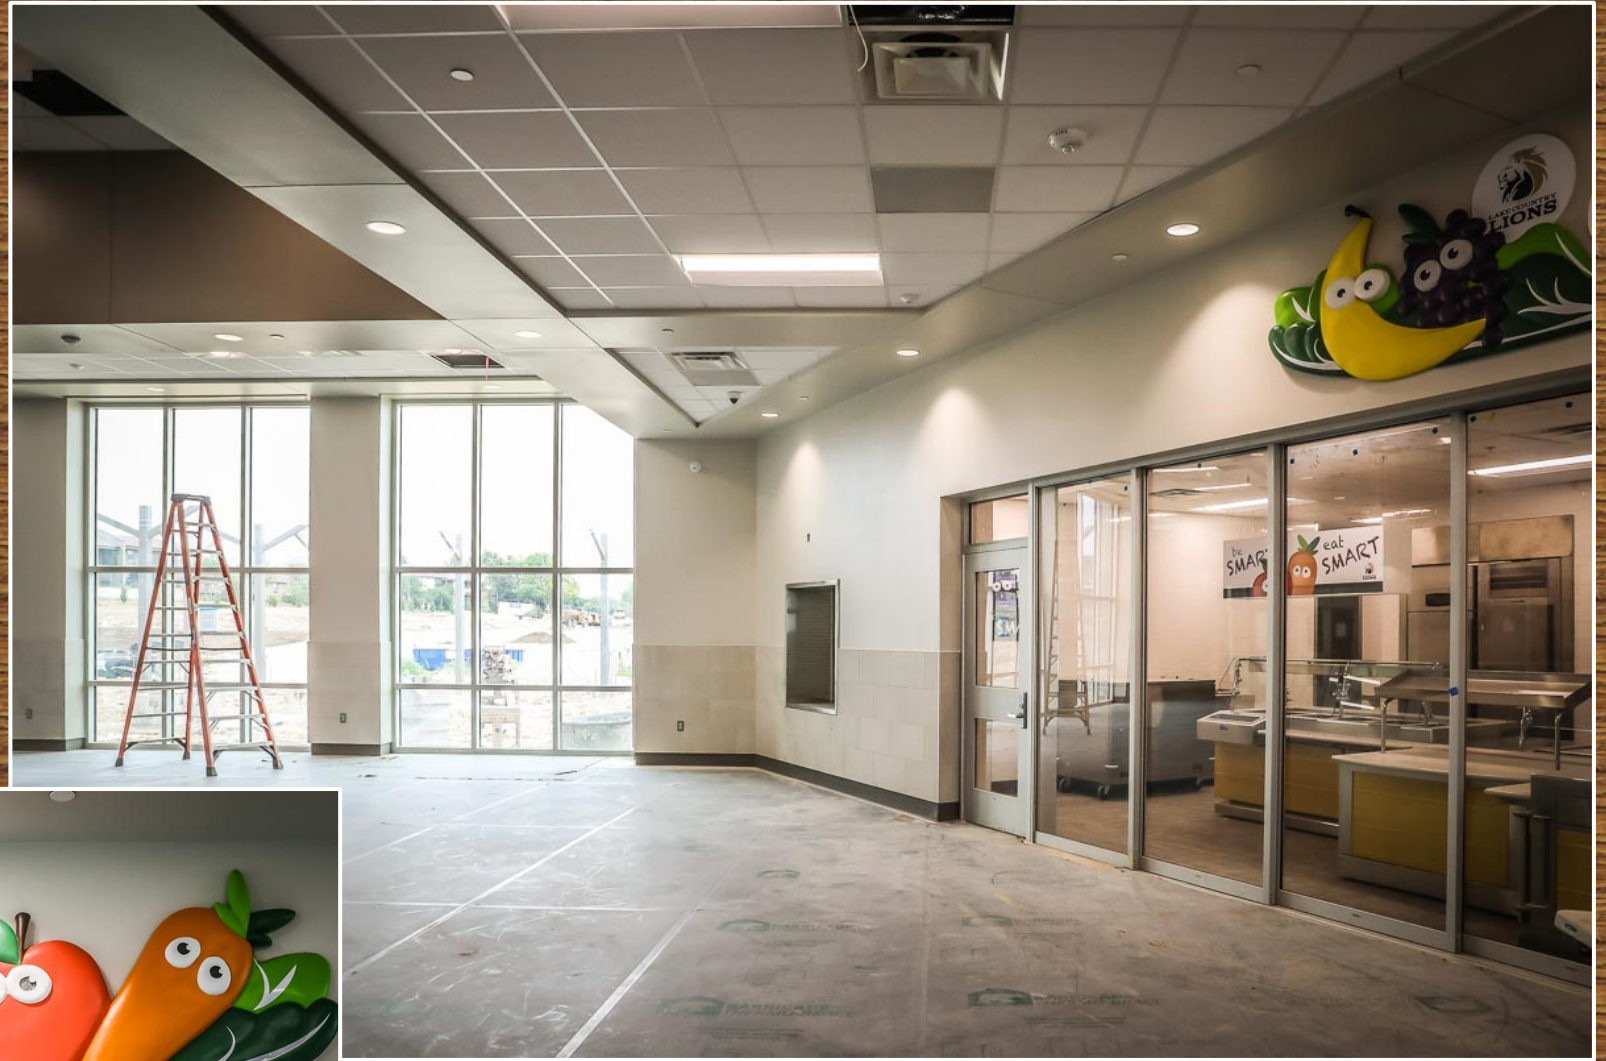





Office area is 95% complete. Upstairs classrooms ceiling grid have been installed. Final above ceiling inspection is needed before panels can be dropped in place. The main corridor is complete except for flooring and sound panels.

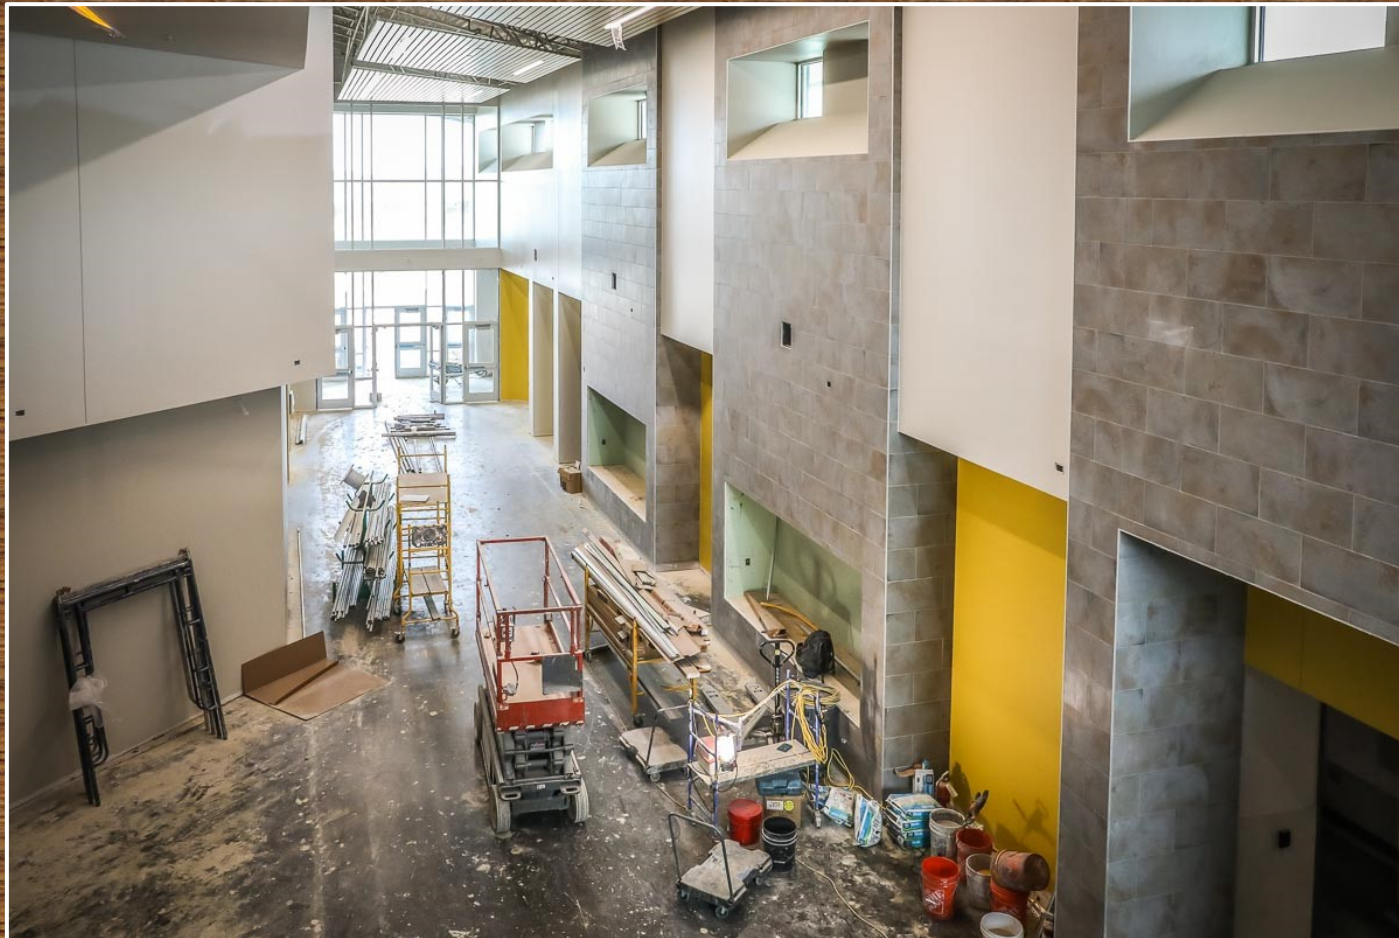



Gym basketball goals are being installed. Second grade hallway is being prepped for VCT. 80% of the classrooms have carpet installed.





**Rain has caused a delay in pouring sidewalks, which needs to be completed before playground installation can occur.**



# CHISHOLM TRAIL HS AND SAGINAW HS



**Baseball fields turf projects are in the beginning stages of moisture conditioning.**
