


EAGLE MOUNTAIN HS



Courtyard sunset



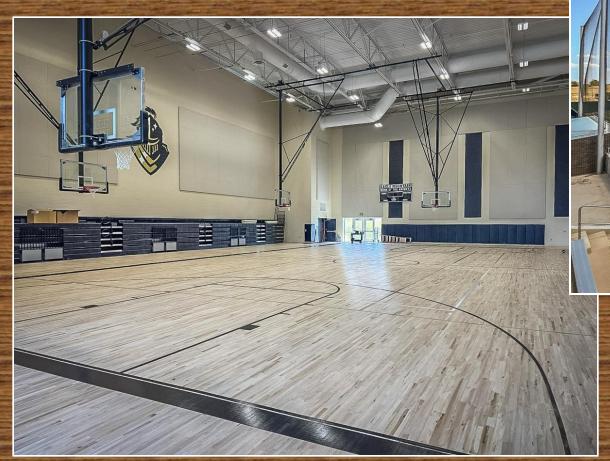



- Upper basketball gym striping is complete.
- Baseball turf infill is in progress. Turf to be completed by August 19.



WAYSIDE MS UPDATE

- Building pad prep is ongoing.
- Pier drilling is scheduled to start by the end of August.
- Geothermal well drilling to start at the beginning of September.







SUMMER PROJECTS

 HVAC equipment replacements at Highland MS, Creekview MS, and Saginaw ES are complete.

Security buzz-in system has been installed at all secondary campuses.



PLAYGROUND RESURFACING PROJECT





 Bryson ES, Comanche Springs ES, Chisholm Ridge ES, Elkins ES, Gililland ES, High Country ES, and Northbrook ES playground turf is complete.



PLAYGROUND RESURFACING PROJECT













 Exterior improvements for Chisholm Ridge ES,
Comanche Springs ES, and Eagle Mountain ES are complete.















 Exterior improvements for Prairie Vista MS,
Parkview ES,
Northbrook ES, and
Remington Point ES are complete.








 Saginaw HS and Willow Creek ES landscaping is complete.





SAGINAW HS CONCRETE PROJECT

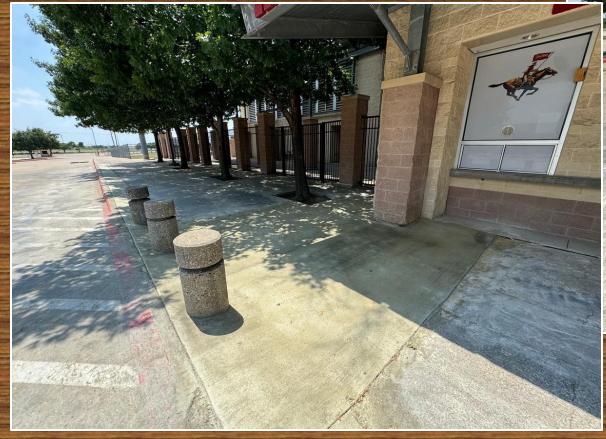



The concrete project is complete at Saginaw HS.



GILILLAND ES COURTYARD PROJECT





 Landscaping is complete at the Gililland ES courtyard. Stone benches to be provided and fencing to be replaced at transformer enclosure.




GYM FLOOR PROJECT



Gym floors at Boswell HS, Lake Pointe ES, Comanche Springs ES,
Chisholm Ridge ES, Remington Point ES, Northbrook ES, and
Parkview ES are complete.



GYM FLOOR PROJECT

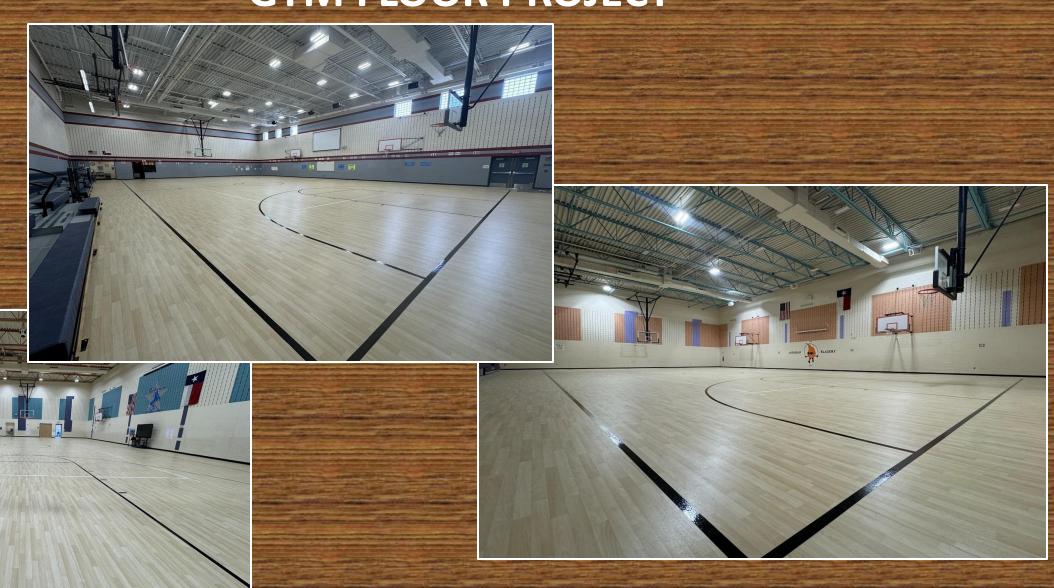



TRAFFIC SIGNAL AT MARINE CREEK PARKWAY

- All lights have been installed.
- Once Oncor sets meter, testing and programming of traffic lights to follow.
- Still scheduled to be up and running by the end of August.
